GROUP ASSIGMENT

Project Management Services for KTH's 200th anniversary

Prepared for:
Rodolfo Palomino Jimenez
William Pääjärvi
Thejas Urs
Thayawee Suchatchit

Content

1 Project plan 4
1.1 Executive summary 4
1.2 Background, purpose and goal 4
1.2.1 Background 4
1.2.2 Purpose 5
1.2.3 Goal 5
1.3 Project Scope 5
1.3.1 Scope 5
1.4 Requirement specification 6
1.4.1 Product specification 6
1.4.2 Project specification 6
1.4.3 Prerequisites 6
1.5 Situational analysis and stakeholders 7
1.5.1 SWOT - analysis 7
1.5.2 Conclusions 8
1.5.3 Stakeholder mapping 8
1.6 Organization and roles 9
1.6.1 Roles, responsibilities and authorities 9
1.6.2 Staffing plan 9
1.7 Communication 10
1.7.1 Reports and documents 10
1.7.2 Communication plan 10
1.8 Milestones 12
1.8.1 Milestone plan 12
1.9 Activities 12
1.9.1 Activity list 12
1.10 Schedule / Bar chart 13
1.10.1 Schedule / Bar chart 13

1.11 Project budget 13
1.12 Risk analysis and response planning 14
2 Appendixes 16
2.1 Work Breakdown Structure (WBS) 16
2.2 Stakeholders Mapping 18
2.3 Project Planning 20
2.4 Project Planning and milestones 22
2.5 Milestones map 24
2.6 Schedule planning 26
2.7 Network diagram 27

1 Project plan

Project name: KTH Throughout History

Client / Sponsor: KTH Jubilee Office/ KTH University

Project manager:

1.1 Executive summary

A short summary of the project plan

The project consists of a full-day event at KTH Borggården to commemorate the university's 200th anniversary.

It begins with an opening ceremony, including an introduction and speech by the King of Sweden.

The main program is structured into seven historical eras (stations) from 1827 to the present, each with themes, visuals, music, and immersive activities that showcase KTH's evolution.

Students or visitors, tour stations with guides in costume or supported by AR/VR elements, receive stamps in a "student passport," and have optional mini lectures in each station.

1.2 Background, purpose and goal

1.2.1 Background

Description with a clear and defined connection to the goal and the business value

The project is part of the commemoration of KTH's 200th anniversary in 2027, a historic occasion that seeks to highlight the university's legacy and its role in Sweden's technological, scientific, and social development. The celebration, including the opening ceremony in the presence of the King of Sweden, will reinforce KTH's institutional relevance.

The central objective is to ensure high satisfaction among key stakeholders, including authorities, the academic community, students, and external partners, while enhancing KTH's reputation and visibility nationally. The event not only commemorates the institution's history but also clearly communicates its values of innovation, sustainability, and academic excellence.

By increasing its prestige, KTH strengthens its institutional brand, generating tangible strategic value: attracting future students, consolidating ties with prestigious

researchers, and establishing alliances with strategic partners. In this way, the project directly contributes to improving KTH's positioning.

1.2.2 Purpose

The impact the project is expected to create, i.e., why it is important to execute the project

The project's purpose is to celebrate KTH's 200th anniversary with an event that strengthens the university's reputation and visibility nationwide, while ensuring high satisfaction among key stakeholders through a meaningful cultural and historical experience.

- **Hight satisfaction of the stakeholders**
- **Potential to enhance KTH's reputation and visibility**

1.2.3 Goal

What should be achieved when the project is executed.

Organize a one-day event at Borggården in 2027 to celebrate KTH's 200th anniversary, ensuring the participation of at least 1,000 attendees and the satisfaction of 90% of key stakeholders.

1.3 Project Scope

1.3.1 Scope

What is included as part of the project and must be performed in order to deliver the goal(s).

The project covers the planning, organization and execution of our event KTH Throughout History. This is to celebrate KTH's 200-year anniversary and will be held in Borggården. The scope requires some specific functions to be able to happen.

The main work packages are:

1.1 Ceremony, which covers the official opening, stage preparation, and the King's speech.

1.2 Art, which develops visual exhibitions across KTH's historical eras

1.3 Music, which provides musical performances reflecting each era

1.4 Equipment, which ensures sound, lighting, displays, and safety infrastructure are in place

1.5 Guests, which manages invitations, VIPs, and audience services

1.6 Staff, which organizes the project team, technical crew, and service personnel

1.7 Logistics & Venue, which handles permits, seating, restrooms, waste management, and overall venue setup

1.8 Security, which ensures safety for attendees and VIPs through screening, coordination, and protective measures

1.9 Communication & Marketing, which manages invitations, promotions, press, website, and social media

2.0 Finance & Administration, which oversees budgeting, contracts, and insurance.

1.4 Requirement specification

1.4.1 Product specification

Requirements on the project's results

The project is a one-day event celebrating KTH's 200-year anniversary. The product is a historical and art exhibition divided into seven areas. These areas are different time periods of KTH's history, they will be represented with their own art and music. The event includes a starting official ceremony with a speech of the King of Sweden. The result shall be an immersive, informative, safe and engaging event for all guests.

1.4.2 Project specification

Requirements on the execution and prioritization between the project's triple constraints

The project must be completed within the timeframe and allocated budget. The scope, time and cost have to be balanced to create a quality event. This is done by keeping the scope in check. Security will be a vital component because of the Kings presence. The execution requires coordinated planning of the logistics, staffing, venue setup, communication and marketing. These must be up to standard and follow safety regulations to make the event of high quality.

1.4.3 Prerequisites

Demands on the project's sponsor/owner or client that have to be achieved to ensure the project's execution and result.

The project will require the support and approval from KTH and also external authorities. We need to get permission for permits, funding and security. There will also be cooperation with the royal court for the event. The suppliers of equipment, art,

music, staff and such will have to be engaged in advance to ensure that the event can occur. Financial resources from KTH will have to be secured to cover the costs. Commitment from staff and volunteers will also be a key to its success.

1.5 Situational analysis and stakeholders

1.5.1 SWOT - analysis

Mapping and analysis of external and internal factors that might affect execution. The complete SWOT analysis should be included as an attachment.

Strengths	***Weaknesses***
• ***Prestigious setting****: Historic KTH Borggården and presence of the King of Sweden add prestige, credibility, and visibility.* • ***Unique concept****: Seven historical eras with immersive activities, music, visuals, and costumes create an engaging, memorable experience.* • ***Integration of technology****: AR/VR elements modernize the storytelling and appeal to tech-savvy students and visitors.* • ***Educational value****: Mini lectures and the "student passport" system add interactive learning and cultural enrichment.* • ***Institutional pride****: Celebrates KTH's legacy and achievements over 200 years, strengthening alumni, student, and faculty connections.* • ***Media attention****: Likely to attract strong press coverage due to the anniversary and royal presence.*	• ***Complex logistics****: Coordinating multiple stations, costumes, guides, and AR/VR tech can be resource-intensive and prone to technical or timing issues.* • ***Cost****: High budget requirement for staging, security (due to the King), technology, costumes, and event management.* • ***Weather dependency****: Outdoor location at Borggården poses risks if the weather is poor.* • ***Visitor flow management****: Ensuring smooth transitions between stations to avoid congestion or uneven participation could be challenging.* • ***Limited accessibility****: AR/VR or certain immersive elements might exclude older or less tech-savvy visitors.*
Opportunities	***Threats***
Showcasing innovation*: Event highlights KTH as a forward-looking university blending history with future-oriented tech (AR/VR, immersive learning).* ***Strengthening partnerships:*** *Opportunity to engage government, industry, and alumni.* ***Tourism and branding****: Can attract international attention, strengthening KTH's global brand as a leading technical university.* ***Student engagement****: Involvement of students as guides, performers, or tech support builds community and enhances their learning experience.*	***Security risks****: Presence of the King requires heightened security; any lapse could overshadow the celebration.* ***Technical failures****: AR/VR glitches, sound/visual breakdowns, or passport-stamp logistics issues may disrupt the flow.* ***Public criticism:*** *Perceptions of high spending on celebrations instead of education or research could cause negative press.* ***Low participation****: If poorly marketed, attendance could be lower than expected, reducing impact.*

***Digital extension**: Content can be live-streamed or repurposed online for broader reach, creating a lasting digital archive.* ***Cultural impact:** Strengthens connections between academia, arts, and Swedish history.*	***External disruptions**: Political events, protests, or unforeseen crises could interfere with the event.* ***Health/safety concerns:** Large crowds raise risks of accidents, illness, or logistical bottlenecks.*

1.5.2 Conclusions

KTH's 200th anniversary event presents a unique opportunity to reinforce the university's image as a modern, innovative institution steeped in history. Its main strengths lie in the prestige of the venue, the participation of the King, and the use of immersive technology that appeals to diverse audiences. However, the project also faces significant challenges such as high costs, logistical complexity, and weather dependence. If security, organization, and communication are well managed, the event can have a strong positive impact on KTH's reputation and strengthen ties with students, partners, and the wider community.

1.5.3 Stakeholder mapping

Mapping and analysis of individuals, groups and organizations that might affect the project or will be affected by the project.

Note: Refer to Stakeholder mapping Appendix 2.2

Core stakeholders	
KTH Administration/Management	*The objective is to make use of the funds properly, align the event to the institutions goal and safeguard KTH's reputation*
Invited artists and musicians	*The objective is to showcase talent and build network with academia*
Student Union (THS)	*The objective is to increase the engagement among the student community*
Primary stakeholder	
Students	*The objective is to make the enjoy and contribute to the cultural events happening on campus*
Sponsors	*The objective is to promote their brand and strengthen their ties with KTH*
Faculty and Researchers	*The objective is to ensure that the event reflects KTH's educational and scientific legacy.*
Secondary stakeholders	

General public	*The objective is to enjoy the public event*
Government and Authority	*The objective is to maintain order*

1.6 Organization and roles

1.6.1 Roles, responsibilities and authorities

Organizational structure that specifies project roles, actor's authority and responsibilities.

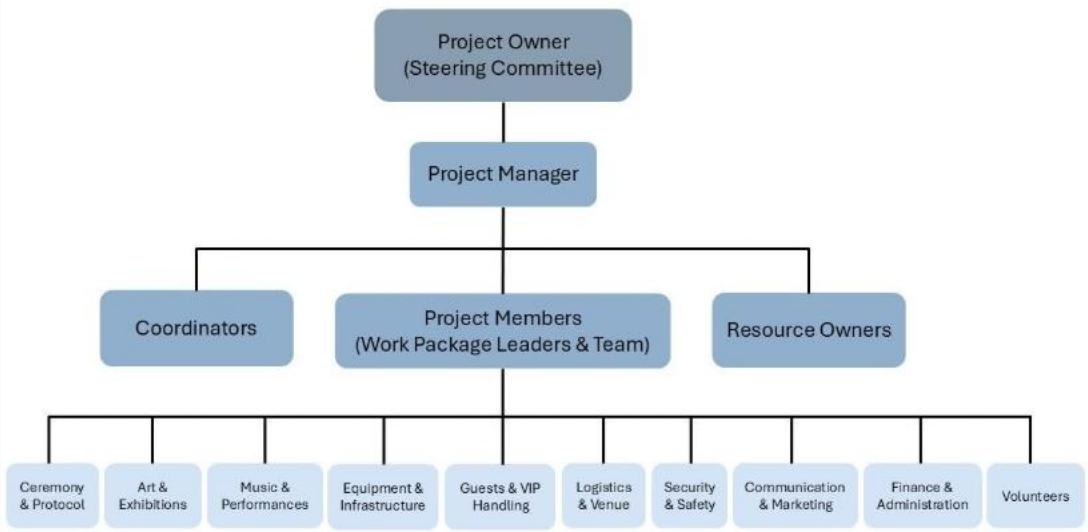

The project is organized with a clear hierarchy to separate decision-making, management, and execution. At the top, the project owner (steering committee) provides strategic direction, approves the budget, and ensures alignment with institutional goals. The project manager organizes and coordinates activities, manages resources, and leads the project group. At the operational level, project members (work package leaders and teams) execute tasks, report progress, and deliver outputs in line with project standards. Coordinators facilitate communication across work packages, while resource owners contribute specialized expertise or provide necessary resources. Volunteers strengthen execution by supporting logistics, guest services, and communication. This structure ensures accountability, efficiency, and coordination across all project dimensions.

1.6.2 Staffing plan

What staff is needed to successfully carry out the project? Who is given which role in the project.

Staffing for the project is designed to ensure that the right resources and competences are available at the right time. The Project Manager will request the type and number of resources needed, while resource owners or line managers will provide suitable staff.

Internal staff from KTH will be used where possible, while external suppliers and specialists (such as stage technicians, security staff, and performers) will be recruited where necessary. The project team will include coordinators, technical crew, designers, musicians, artists, and volunteers, with roles allocated according to competence and availability. The Project Manager will have the final say on team composition to ensure effective collaboration and team chemistry. Resources needed later in the project, such as additional service staff or guest management personnel, will be allocated in advance to ensure they are available when required.

1.7 Communication

1.7.1 Reports and documents

Rules and routines on how to follow up and report on the project's progress.

The project will follow clear rules and routines to ensure effective follow-up and reporting. The Project Manager will prepare progress reports for the Steering Committee at decision points and in monthly meetings, with weekly reports in the final phase before the event. The Project Members, including work package leaders, will provide weekly updates on tasks, resources, and potential risks, and any major deviations will be reported immediately. The Project Owner will receive summary reports at key milestones to confirm alignment with project goals and to approve major decisions. Financial reports covering budget status, payments, and contracts will be prepared monthly and more frequently near the event. Risk and safety documentation, including permits and contingency measures, will be updated continuously and reviewed before handover to authorities. All reports and documents will be stored in a shared project platform, and a final evaluation report will be produced after the event to summarize results, lessons learned, and recommendations for future projects.

1.7.2 Communication plan

Plan for spreading information for the purpose of making sure that the right target group gets the right information at the right time and through the right channels.

The communication plan ensures that each target group receives the right information at the right time and through the right channel. The Steering Committee will be informed about project status, budget, and risks at decision points and in monthly meetings, while the Royal Court and King's Office will receive protocol details and security information early and continuously until the opening ceremony. The Project Team will be updated weekly and daily in the last week to align tasks and resources, and performers such as artists and musicians will be given rehearsal schedules, stage instructions, and briefing notes after contracting and before the event. Suppliers and

contractors will receive specifications, schedules, and site access information at contract signing and milestone dates, while volunteers and service staff will be trained before the event and briefed daily during execution. Sponsors and media partners will be updated through press releases, media kits, and events at agreed PR dates, while guests and the general public will be informed through invitations, the website, social media, printed programs, and signage. Authorities such as police, fire department, and city council will be provided with permit applications, safety documents, and risk assessments early and before the event. Finally, the Finance and Administration team will receive regular budget, and contract reports monthly and weekly before the event. This approach guarantees clear, timely, and targeted communication across all stakeholders.

Who	Why	What	When	How	Responsible
Steering committee	Will the project be delivered as planned?	Project status, budget, risks	At decision points, monthly	Meetings, reports	Project manager
Royal Court / King's Office	Confirm participation, protocol	Ceremony agenda, security needs	Early and ongoing until event	Official correspondence, protocol meetings	Project owner
Project team (coordinators, technicians, designers, musicians, artists, volunteers)	To plan and deliver tasks, performances, and technical setups	Tasks, schedules, rehearsals, resources	Weekly during planning, daily in final week, plus rehearsals before event	Meetings, rehearsal schedules, task tools, briefing notes	Project manager
Suppliers & contractors	Ensure delivery/installations	Specs, schedules, site access	At contract and milestones	Contracts, kickoff, coordination meetings	Project member
Sponsors & media	Visibility and PR	Benefits, press updates	At sponsorship signing, PR dates	Press kits, releases, events	Project manager
Guests & public	Clear info, smooth experience	Program, entry info, activities	Pre-event, event day	Website, social media, printed programs, signage	Project member
Authorities	Ensure safety and compliance	Permits, safety and risk plans	Early and before event	Applications, safety briefings	Project manager
Finance & administration	Control costs and contracts	Budget, payments, insurance	Monthly, weekly near event	Reports, finance meetings	Project manager

1.8 Milestones

1.8.1 Milestone plan

An overarching flow chart or table of the project's most important milestones (start from the WBS structure)

Note: Refer to Milestone planning Appendix 2.4

1.9 Activities

1.9.1 Activity list

List of activities where time and resources are estimated (start from the WBS structure)

Note: It is assumed that the project will start on January 2, 2027, but this date may be modified according to the date of the event.

Note: Refer to Schedule planning and Project planning Appendix 2.3, 2.4 and 2.6

ID	Activity	Resources	Start	Stop
1.1.1	Prepare scene	4	19-03-2027	22-03-2027
1.1.2	Arrange for Ceremony security	2	15-01-2027	20-01-2027
1.1.3	Kings' speech	1	23-03-2027	23-03-2027
1.1.4	Arrange for ceremony band	1	12-03-2027	18-03-2027
1.2	Finalizing the Art	2	26-02-2027	11-03-2027
1.3	Finalizing music	2	26-02-2027	11-03-2027
1.4	Arranging equipment for music, lights, exibitional material, safety equipment, Power and infrastructure	3	29-01-2027	25-02-2027
1.5	Inviting the Guests	2	07-01-2027	07-02-2027
1.6	Arranging the staff for different sections of the ceremony	2	15-01-2027	24-01-2027
1.7.1	Obtaining permits	1	07-01-2027	14-01-2027
1.7.2	Setting up Borggården	4	25-01-2027	28-01-2027
1.7.3	Seating	2	29-01-2027	01-02-2027
1.7.4	Waste management setup	2	29-01-2027	31-01-2027
1.8	Arranging for the security	2	15-01-2027	20-01-2027
1.9	Marketing activities	3	07-01-2027	03-02-2027
2.0	Budgeting and contracts	2	02-01-2027	06-01-2027

1.10 Schedule / Bar chart

1.10.1 Schedule / Bar chart

Activity plan with a time axis where duration and connection between activities and milestones are shown.

Note: Refer to Schedule planning Appendix 2.6

1.11 Project budget

Category	Amount	Cost (SEK)	Comments
Total Internal costs		**369,900.83**	
Internal staff / coordination		148,598.40	
Hours planned	736		
Average hourly earnings (excl. taxes)		201.90	SCB - Professional, scientific and technical activities
Art & exhibition		38,416	
Hours planned	224		
Average hourly earnings (excl. taxes)		171.50	SCB - Arts, entertainment and recreation
Music / Performances		38,416	
Hours planned	224		
Average hourly earnings (excl. taxes)		171.50	SCB - Arts, entertainment and recreation
Ceremony band		9,604	
Hours planned	56		
Average hourly earnings (excl. taxes)		171.50	
Budget & contract administration		22,880	
Hours planned	80		
Average hourly earnings (excl. taxes)		286	Average financial advisor in Sweden
Total (excl. taxes)		257,914.40	
Tax – Arbetsgivaravgiften (%)	31.42%	81,036.70	
Tax – Semesteravgift (%)	12.00%	30,949.73	
Total (incl. taxes)		369,900.83	
Total External costs		**831,267.38**	
Equipment & infrastructure		260,848	
Hours planned	1,120		
Average hourly earnings (excl. taxes)		232.90	SCB - Construction
Waste management		10,382.40	
Hours planned	48		
Average hourly earnings (excl. taxes)		216.30	SCB - Water supply; sewerage, waste management and remediation activities
Security & protocol		29,472	
Hours planned	96		
Average hourly earnings (excl. taxes)		307	Average health & safety officer in Sweden
Total (excl. taxes)		300,702.4	

Tax – Arbetsgivaravgiften (%)	31.42%	94,480.69	
Tax – Semesteravgift (%)	12.00%	36,084.29	
Total (incl. taxes)		**431,267.38**	
Logistics		75,000	Fixed price
Speaker panel		140,000	
Number of keynote speakers	7		Seven stages, one keynote speaker per stage
Cost per keynote speaker		20,000	Include flights, accommodation and transportation costs
Venue		160,000	Fixed price per venue
Equipment and inventory		25,000	Renting and buying equipment and inventory
Total Other costs		**222,500**	
Marketing		200,000	Including advertisement, communication and ambassadors
Website		20,000	
Consumables		2,500	
Total Bottom-Up Budget		**1,423,668.21**	**SEK**

1.12 Risk analysis and response planning

Risk identification, risk evaluation and Risk response planning.

Risk	Probability 1 to 5	Impact 1 to 5	Risk value = P * I	Risk Response transfer, mitigate, avoid, accept
Wheater disruption	*3*	*4*	*12*	***Transfer/accept:*** *Monitor forecasts and prepare contingency plan, rent tents and tarps that can be mounted in need. Prepare detailed plan on how tarps and tents can be mounted in a stylish and effective way.*
Security breach	*1*	*5*	*5*	***Mitigate:*** *Good coordination with police and the king's security, run drills in advance, careful security checks.*
Technical problems	*3*	*4*	*12*	***Mitigate:*** *Test tech in advance, have prepared technical staff and equipment onsite. Run drills in fixing problems day before.*
Low attendance	*1*	*3*	*3*	***Mitigate:*** *Strengthen marketing, reach out to students, alumni's and others.*
Budget overrun	*3*	*4*	*12*	***Avoid:*** *Keep regular checks with budget, get major expenditures approved in advance, negotiate backup funds from KTH and sponsorships.*
Supplier delays	*3*	*3*	*9*	***Avoid:*** *Confirm and order in advance to provide buffer. Have a strict milestone plan.*

Health incidents	*1*	*3*	*3*	***Mitigate:*** *Have ambulance and medical staff prepared at the event, safety walkthrough to identify and prevent easily avoidable risks.*
Logistical congestion	*3*	*3*	*9*	***Mitigate:*** *Simulate and map the flow of visitors, increase possibility of flow in bottlenecks, send in controlled number of groups into the event. Have staff in an overview position to monitor flow of visitors and provide possibility for communication between overview and security on ground*
Political protests	*2*	*4*	*8*	***Mitigate:*** *Expand the allowed area of event to cover KTH grounds. Discuss permit to disperse crowds that disturb the ordinance of the event. Thorough searches for sabotage and political items during security checks.*

2 Appendixes

2.1 Work Breakdown Structure (WBS)

level 1					**KTH Troughout**	**1.0**														
level 2	**Ceremony**	**1.1**	**Art**	**1.2**	**Music**	**1.3**	**Equipment**	**1.4**	**Guests**	**1.5**	**Staff**	**1.6**	**Logistics & Venue**	**1.7**	**Security**	**1.8**	**Communication & Marketing**	**1.9**	**Finance & Administration**	2.0
level 3	Prepare scene	1.1.1	1827–1877: Founding Era: Art	1.2.1	1827–1877: Founding Era: Music	1.3.1	Stage & sound – speakers, microphones, mixing desk.	1.4.1	VIP management – the King, keynote speakers, special invitees.	1.5.1	Project management – event manager, coordinators.	1.6.1	permits	1.7.1	screening	1.8.1	invitations	1.9.1	budgeting	2.0.1
	Ceremony Security	1.1.2	1877–1910: Industrialization and Growth: Art	1.2.2	1877–1910: Industrialization and Growth: Music	1.3.2	Lighting & decoration – stage lighting, historical decorations.	1.4.2	Guest list – invitations, registrations, RSVPs.	1.5.2	Ceremony staff – host, King's liaison, speech support.	1.6.2	Borggården setup	1.7.2	police coordination	1.8.2	posters	1.9.2	contracts	2.0.2
	The Kings speech	1.1.3	1910–1945: Early Modernization & War Years: Art	1.2.3	1910–1945: Early Modernization & War Years: Music	1.3.3	Exhibition material – display cases, paintings, projectors, VR headsets.	1.4.3	Audience management – tickets, entry, info desk.	1.5.3	Technical team – sound/lighting technicians, IT support.	1.6.3	seating	1.7.3	barriers	1.8.3	website	1.9.3	insurance	2.0.3
	Ceremony band	1.1.4	1945–1960: Post-War Boom & Internationalization : Art	1.2.4	1945–1960: Post-War Boom & Internationalization : Music	1.3.4	Safety equipment – barriers, fire extinguishers, first aid kits.	1.4.4	Guest services – signage, guides, accessibility for disabled visitors.	1.5.4	Service staff – guides, ushers, catering crew.	1.6.4	restrooms	1.7.4			press coverage			
			1960–1980: Social Change & Expansion: Art	1.2.5	1960–1980: Social Change & Expansion: Music	1.3.5	Power & infrastructure – cabling, generators, networking.	1.4.5			Security staff – guards, police coordination.	1.6.5	waste management	1.7.5			social media			
			1980–2000: Digital Revolution: Art	1.2.6	1980–2000: Digital Revolution: Music	1.3.6							emergency exits	1.7.6						
			2000–Present: Modern KTH & Sustainability: Art	1.2.7	2000–Present: Modern KTH & Sustainability: Music	1.3.7														

2.2 Stakeholders Mapping

Stakeholder Mapping

This matrix classifies stakeholders according to Power and Interest

Impact (HIGH)	Interest (LOW)	Interest (HIGH)
Keep Satisfied	**Manage Closely**	
• Government/Authority	• KTH Management • Student Union (THS) • Sponsors	
Monitor	**Keep Informed**	
• General Public • Faculty/Researchers	• Students • Artists/Musicians	

2.3 Project Planning

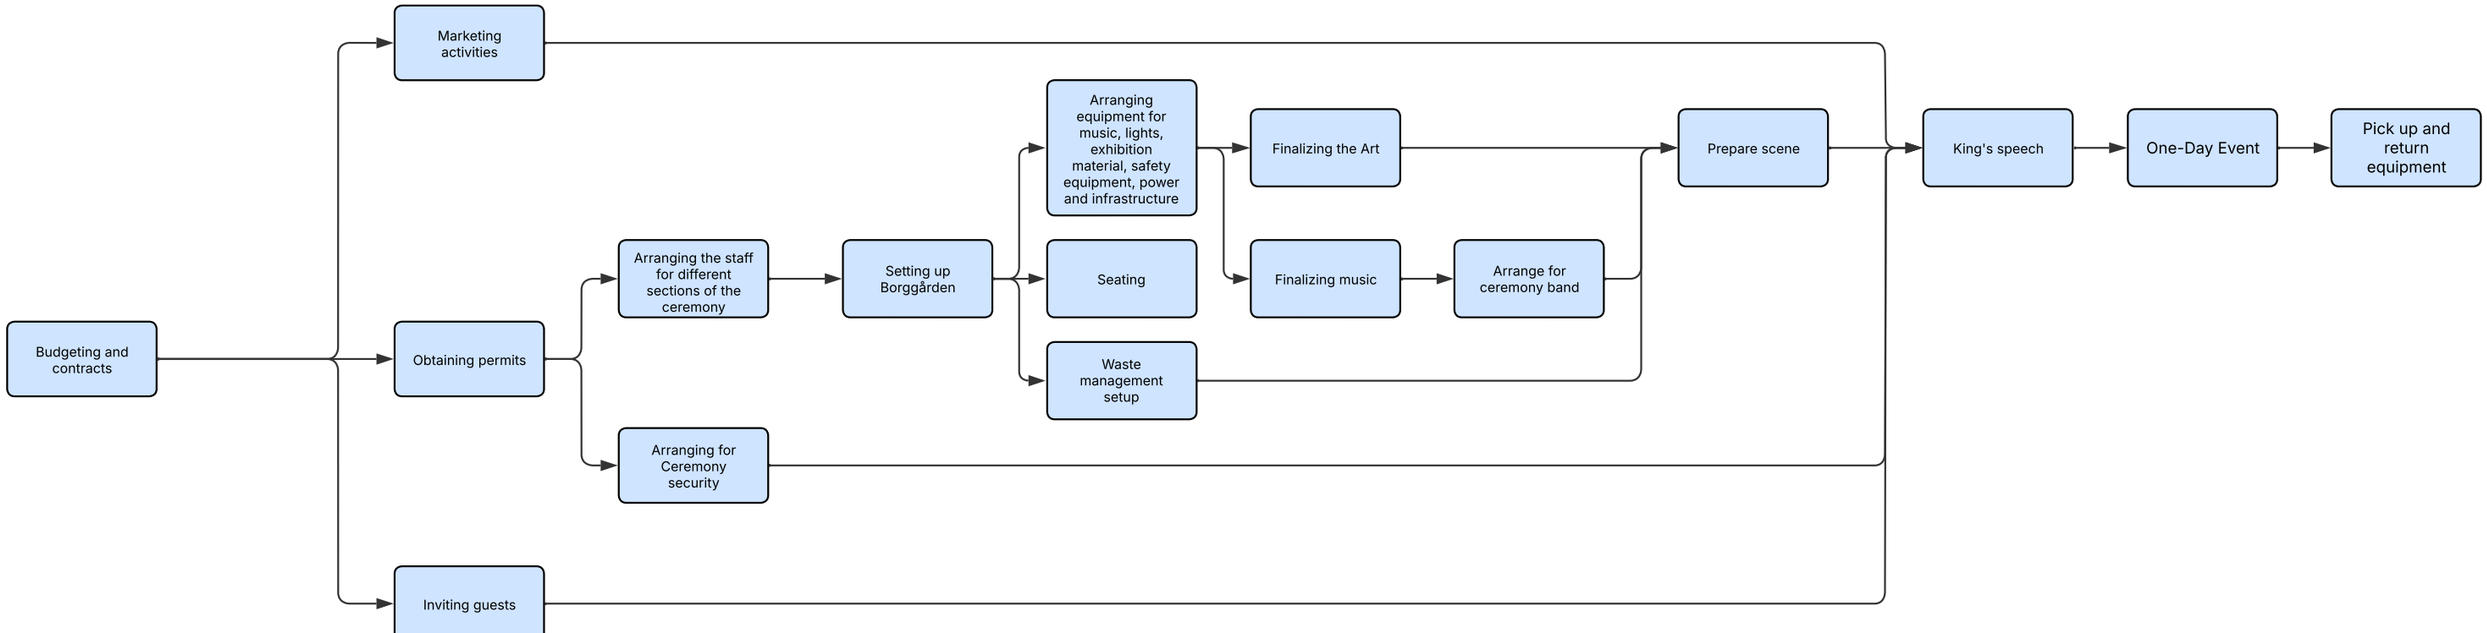
Budgeting and contracts
Marketing activities
Obtaining permits
Inviting guests
Arranging the staff for different sections of the ceremony
Arranging for Ceremony security
Setting up Borggården
Arranging equipment for music, lights, exhibition material, safety equipment, power and infrastructure
Seating
Waste management setup
Finalizing the Art
Finalizing music
Arrange for ceremony band
Prepare scene
King's speech
One-Day Event
Pick up and return equipment

2.4 Project Planning and milestones

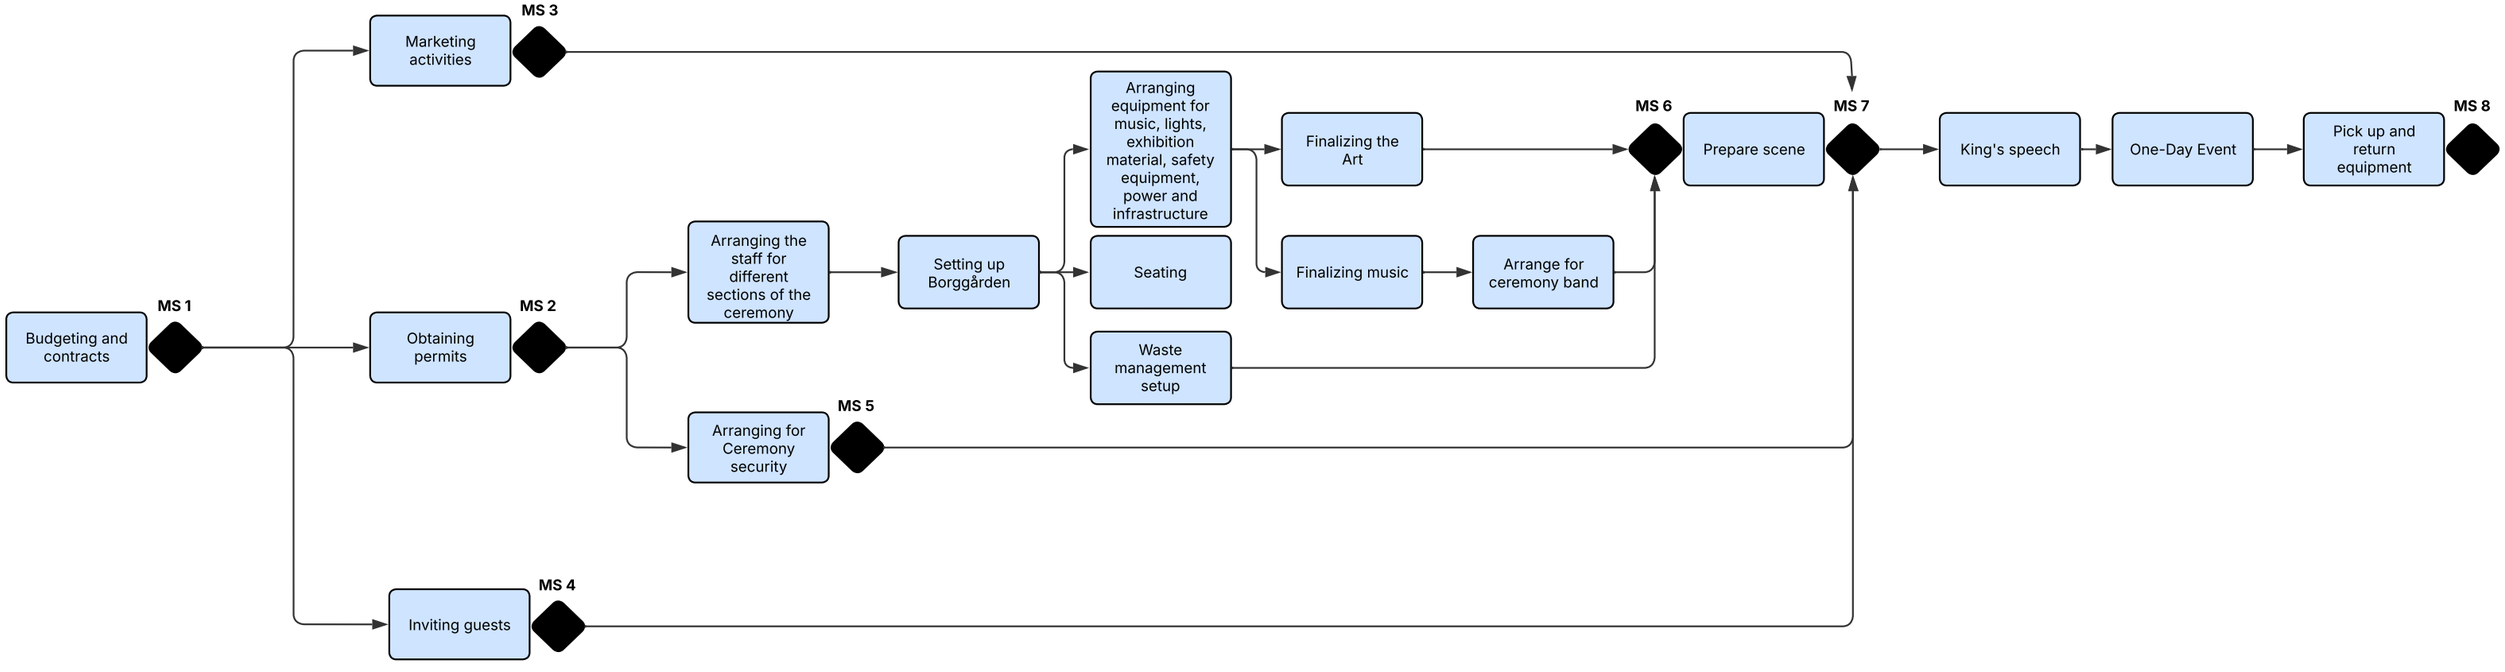

- **Milestone 1:** Budget approved and contracts signed
- **Milestone 2:** Permits obtained
- **Milestone 3:** Marketing completed
- **Milestone 4:** Invitations sent and confirmations received
- **Milestone 5:** Security and staff confirmed
- **Milestone 6:** Art, music and equipment ready
- **Milestone 7:** Ceremony scene prepared
- **Milestone 8:** Project completed

2.5 Milestones map

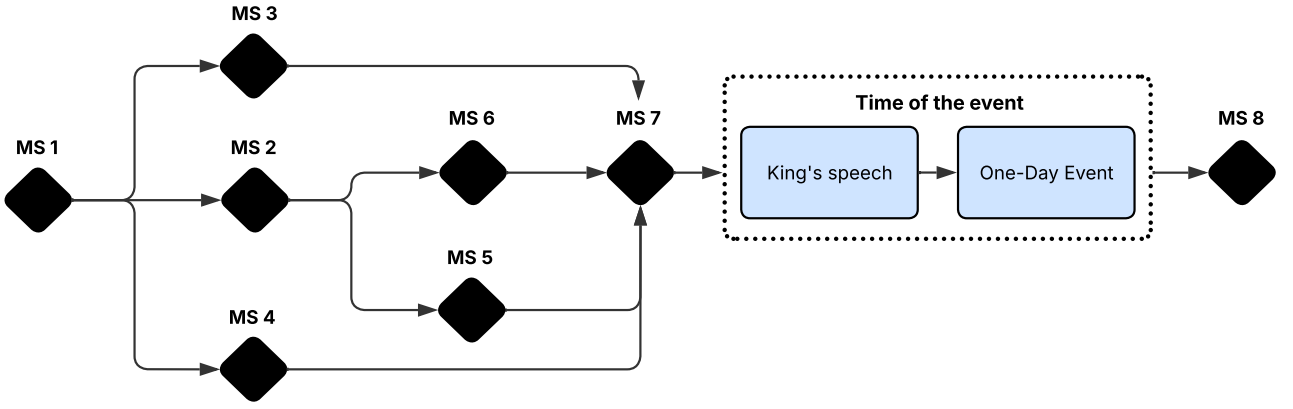

- **Milestone 1:** Budget approved and contracts signed
- **Milestone 2:** Permits obtained
- **Milestone 3:** Marketing completed
- **Milestone 4:** Invitations sent and confirmations received
- **Milestone 5:** Security and staff confirmed
- **Milestone 6:** Art, music and equipment ready
- **Milestone 7:** Ceremony scene prepared
- **Milestone 8:** Project completed

2.6 Schedule planning

Activity list

ID	Activity	Duration (days)	Dependency	Resources (n)	Work time (hours)
1	Budgeting and contracts	5		2	2 x 40=80
MS1	Budget approved and contracts signed		1		
2	Obtaining permits	8	MS1	1	64
MS2	Permits obtained		2		
3	Marketing activities	28	MS1	3	3 x 224=672
MS3	Marketing completed		3		
4	Inviting guests	32	MS1	2	2 x 256=512
MS4	Invitations sent and confirmations received		4		
5	Arranging for ceremony security	6	MS2	2	2 x 48=96
MS5	Security and staff confirmed		5		
6	Arranging the staff for different sections ...	10	MS2	2	2 x 80=160
7	Setting up Borggården	4	6	4	4 x 32=128
8	Arranging equipment for ...	28	7	3	3 x 224=672
9	Seating	4	7	2	3 x 32=64
10	Waste management setup	3	7	2	2 x 24=48
11	Finalizing the Art	14	8	2	2 x 112=224
12	Finalizing music	14	8	2	2 x 112=224
13	Arrange for ceremony band	7	12	1	56
MS6	Art, music and equipment ready		9;10;11;13		
14	Prepare scene	4	MS6	4	4 x 32=128
MS7	Ceremony scene prepared		MS3;MS4;MS5;14		
15	King's speech	0.5	MS7	1	4
16	One-Day Event	0.5	15	20	20 x 4=80
17	Pick up and return equipment	4	16	4	4 x 32=128
MS8	Project complete		17		

Calendar

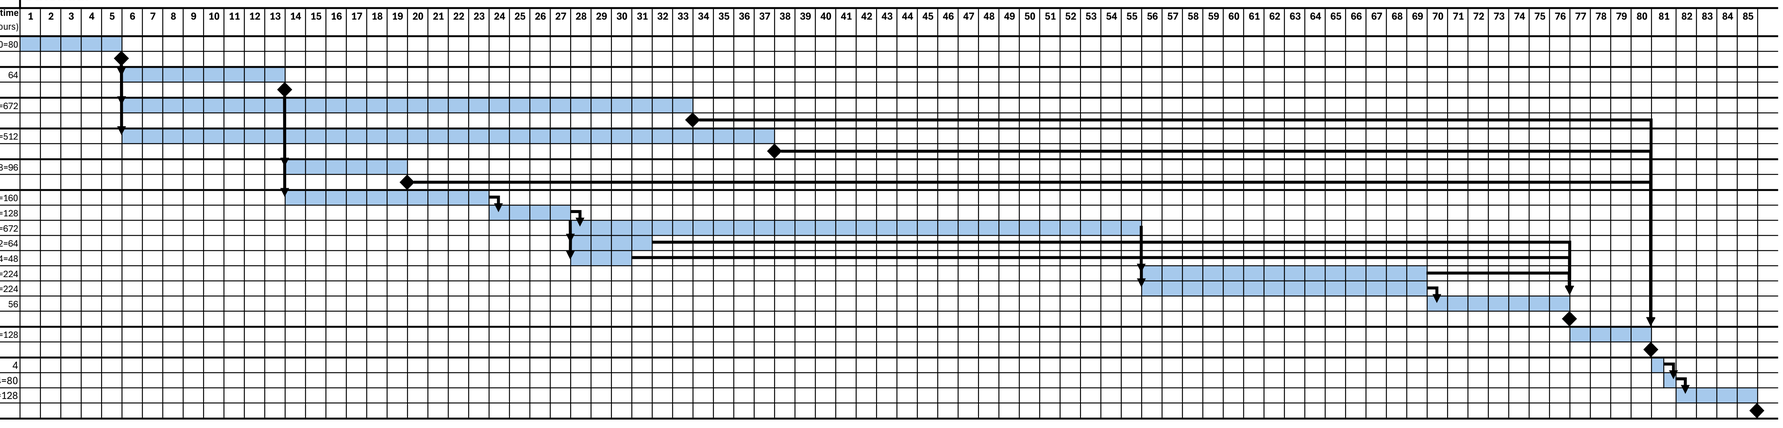

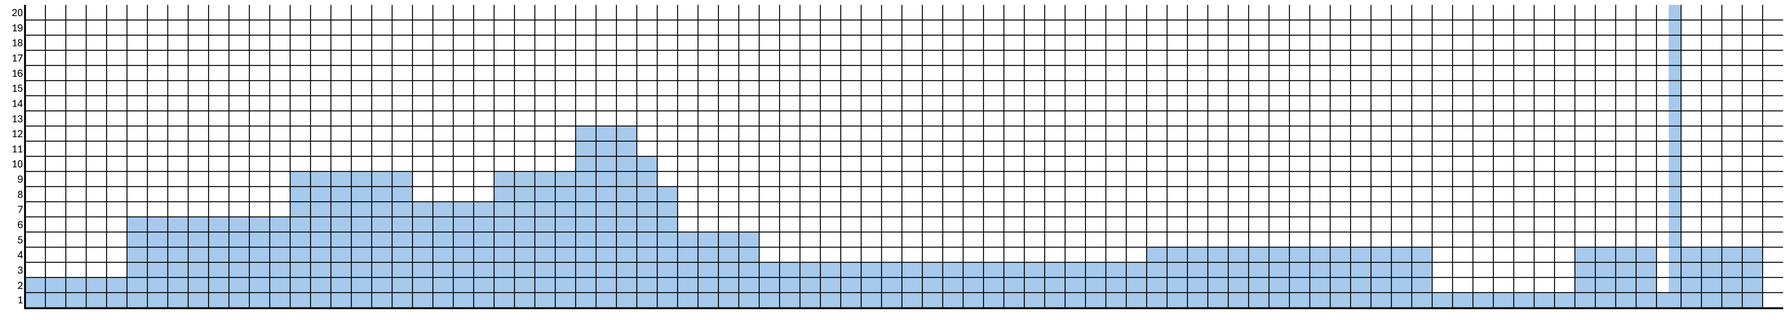

2.7 Network diagram

NETWORK DIAGRAM - KTH Throughout History

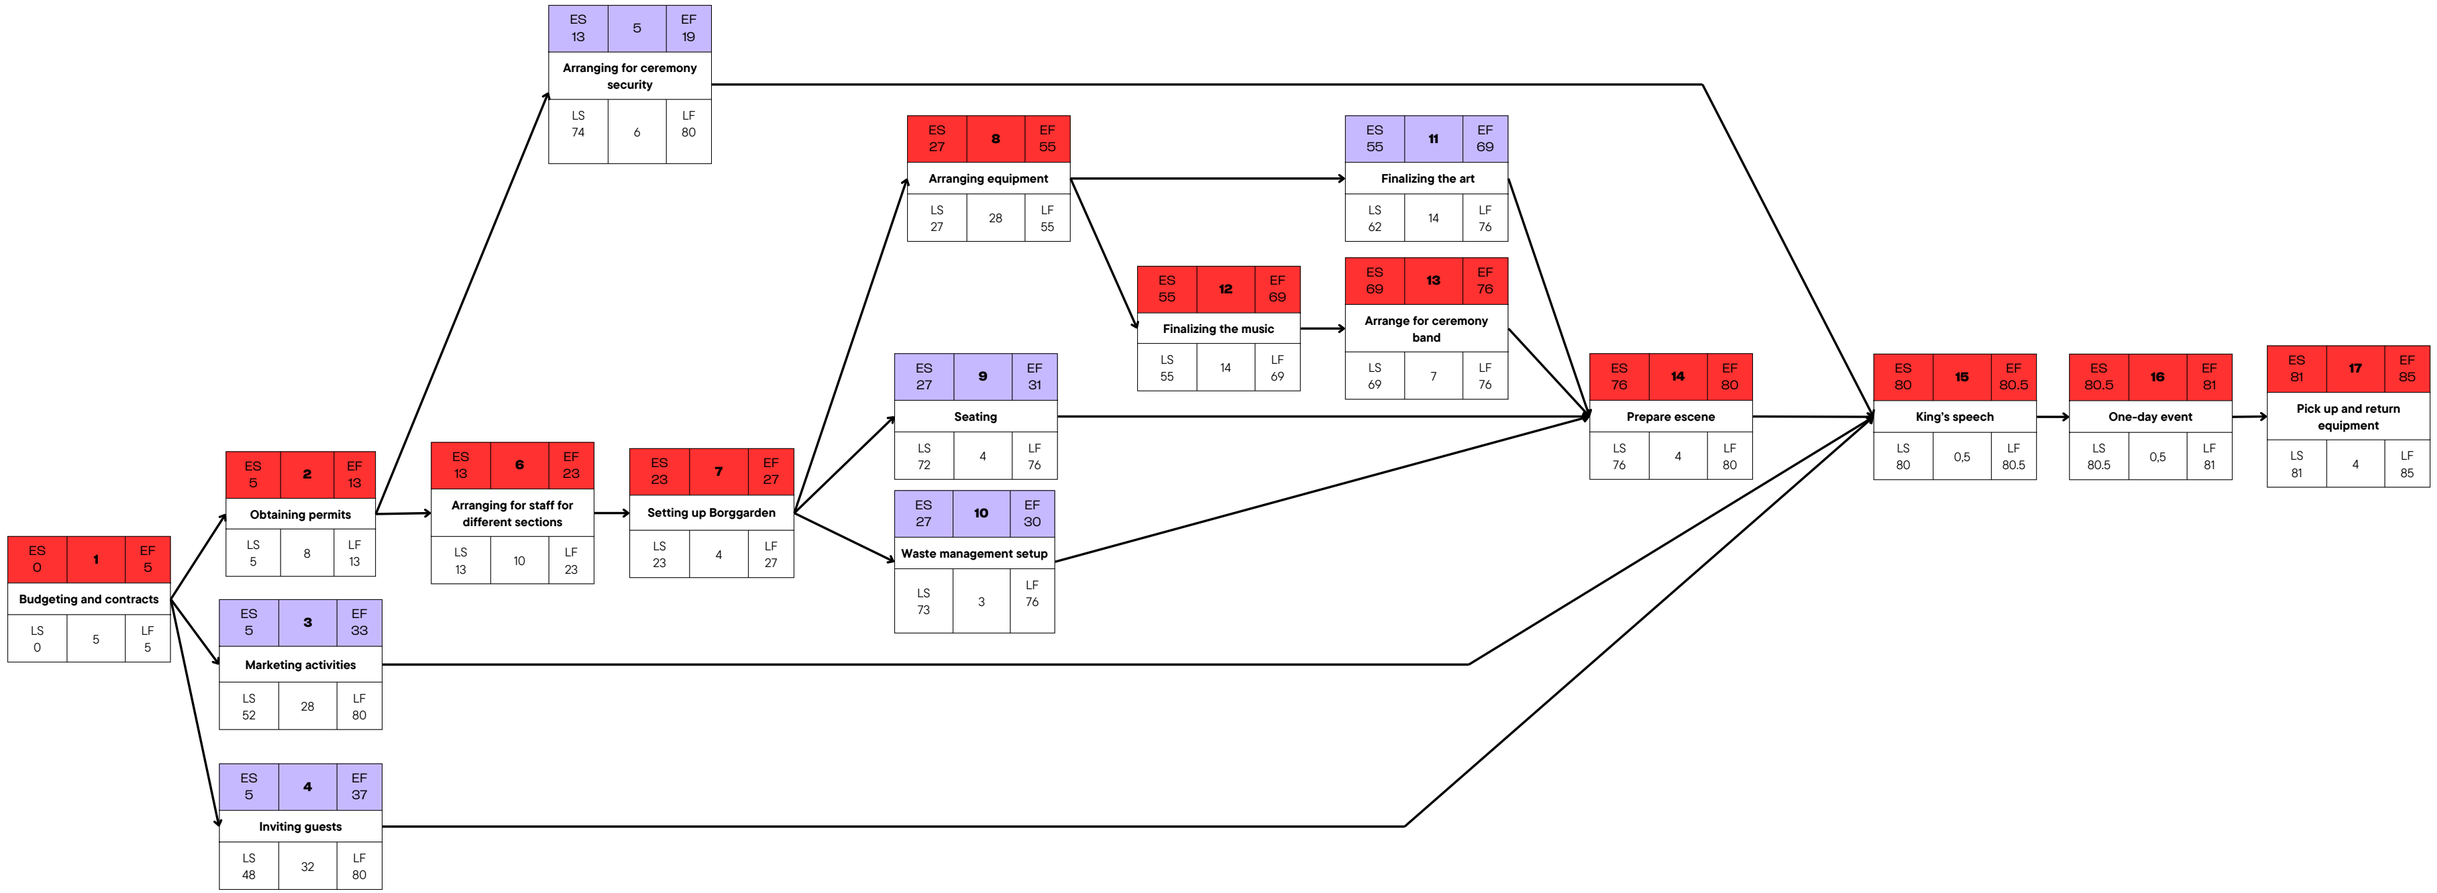

Critical path: 1-2-6-7-8-12-13-14-15-16-17
